ID	Resource Names	Duration	Start	Finish
1	**PRECONSTRUCTION/MILESTONES**	**125 days**	**Wed 5/20/26**	**Tue 11/10/26**
2	PRECONSTRUCTION MEETING	1 day	Wed 5/20/26	Wed 5/20/26
3	PIPELINE SUBMITTALS/PROCUREMENT	20 days	Mon 6/15/26	Fri 7/10/26
4	ISSUE NTP	1 day	Mon 7/13/26	Mon 7/13/26
5	MOBILIZATION/SETUP YARD	1 day	Mon 7/13/26	Mon 7/13/26
6	INSTALL CONST AREA SIGNS	1 day	Mon 7/13/26	Mon 7/13/26
7	INSTALL SWPPP MEASURES	1 day	Mon 7/13/26	Mon 7/13/26
8	UTILITY VERIFICATION	3 days	Tue 7/14/26	Thu 7/16/26
9				
10	**Work Sequence #1 (Pescadero Creek Rd)**	**55 days**	**Fri 7/17/26**	**Thu 10/1/26**
11	4" TW Pipeline (STA 45+00 to STA 113+60) - 6860 LF	25 days	Fri 7/17/26	Thu 8/20/26
12	Install BOV & CARV	2 days	Fri 8/21/26	Mon 8/24/26
13	Install Water Service	2 days	Tue 8/25/26	Wed 8/26/26
14	4" TW Pipeline (STA 94+58 to POPE RD STA 16+04)	2 days	Thu 8/27/26	Fri 8/28/26
15	4" TW Pipeline (STA 11+23 to STA 45+00) - 3377 LF	13 days	Tue 9/15/26	Thu 10/1/26
16				
17	**Work Sequence #2 (Highway 84 La Honda)**	**9 days**	**Mon 8/31/26**	**Thu 9/10/26**
18	4" TW Pipeline (SR-84 STA 19+91 to SR-84 STA 27+11) - 720 LF	5 days	Mon 8/31/26	Fri 9/4/26
19	Concrete Backfill	1 day	Mon 9/7/26	Mon 9/7/26
20	Pull Plates & Pave	3 days	Tue 9/8/26	Thu 9/10/26
21	Install BOV & CARV	1 day	Tue 9/8/26	Tue 9/8/26
22				
23	**Work Sequence #3 (Pescadero Creek Rd --> WTP)**	**2 days**	**Fri 9/11/26**	**Mon 9/14/26**
24	4" TW Pipeline (STA 11+23 to STA 10+00) - 123 LF	2 days	Fri 9/11/26	Mon 9/14/26
25				
26	**Work Sequence #3 (Testing & Disinfection)**	**12 days**	**Fri 10/2/26**	**Mon 10/19/26**
27	Load & Hydrostatic Test 4" TW Pipeline	4 days	Fri 10/2/26	Wed 10/7/26
28	Chlorinate 4" TW Pipeline	4 days	Thu 10/8/26	Tue 10/13/26
29	Dechlorinate & Flush 4" TW Pipeline	4 days	Wed 10/14/26	Mon 10/19/26
30				
31	**Work Sequence #4 (Pipeline Connections)**	**16 days**	**Tue 10/20/26**	**Tue 11/10/26**
32	Excavate & Pipe Waterline Tie-ins	2 days	Tue 10/20/26	Wed 10/21/26
33	4" TW Pipeline Connections	2 days	Thu 10/22/26	Fri 10/23/26
34				
35	CAT-TRACK STRIPING	5 days	Mon 10/26/26	Fri 10/30/26
36	COSM REVIEW CAT-TRACK	1 day	Mon 11/2/26	Mon 11/2/26
37	FINAL STRIPING	1 day	Tue 11/3/26	Tue 11/3/26
38				
39	**PUNCHLIST**	5 days	Wed 11/4/26	Tue 11/10/26

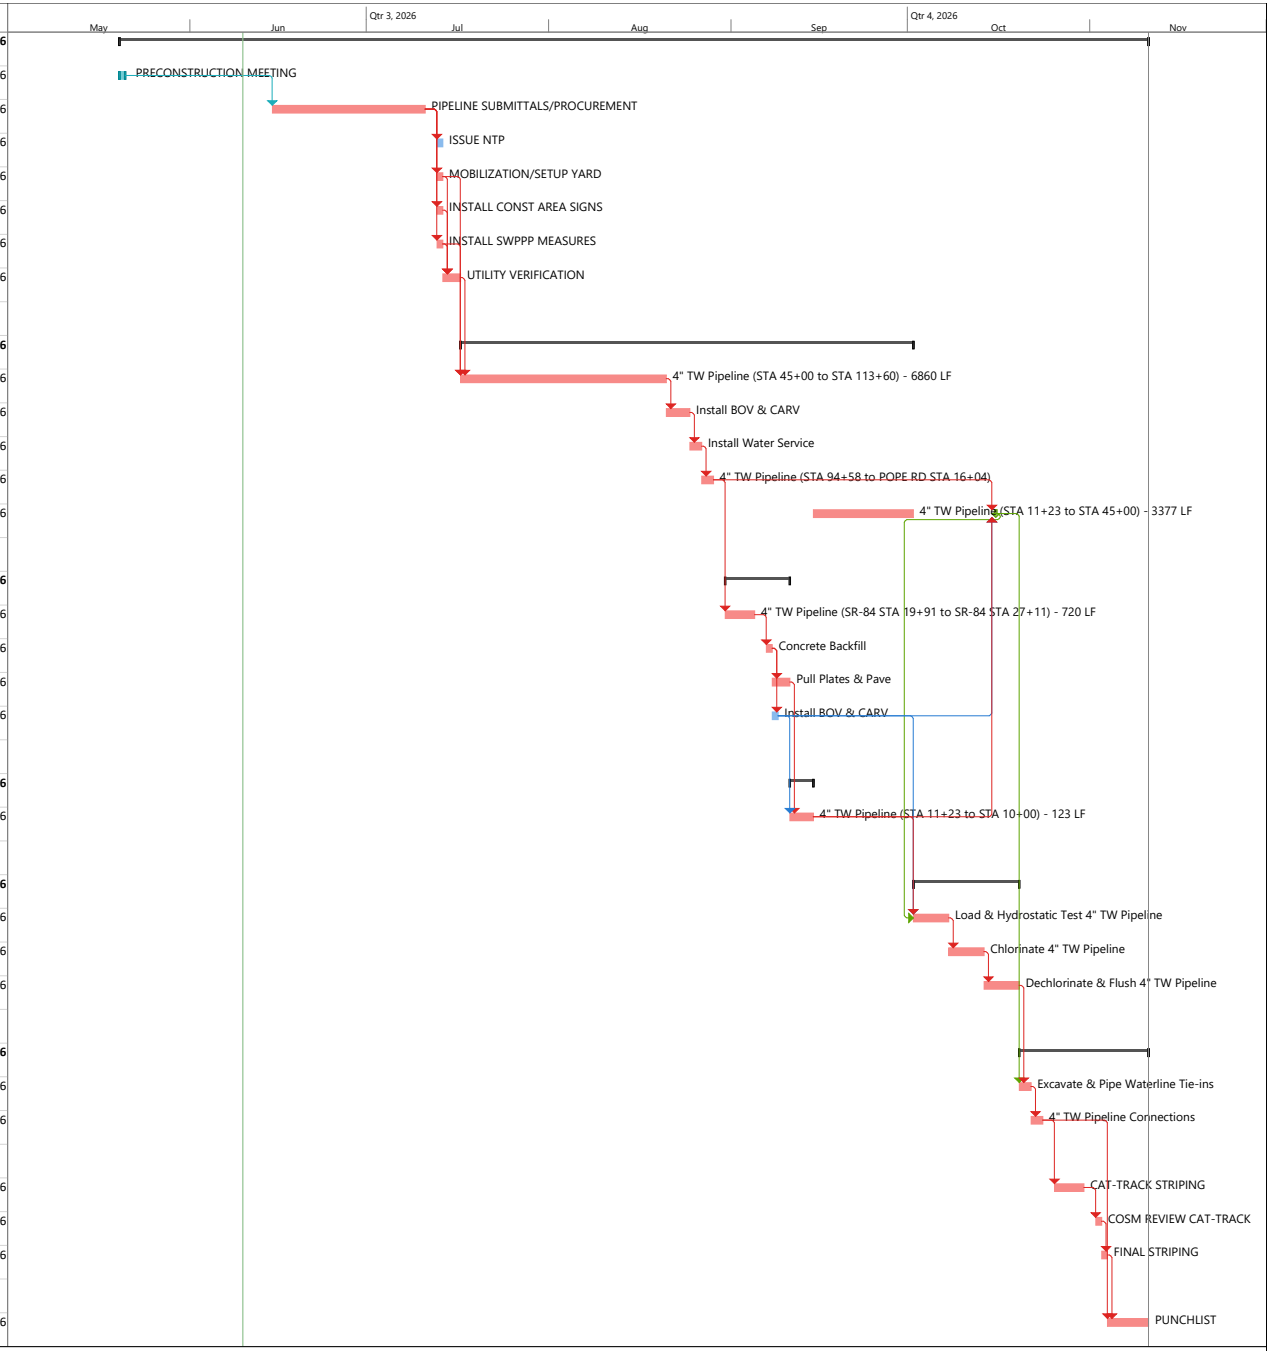

Project: 6203 Baseline
Date: Wed 6/10/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

Schedule is subject to change.
